









[REDACTED]

[REDACTED]

		PROGRAMADO	
MES	FECHA	MES	SEMANTAL
INICIO	23/11/2015		
1	22/12/2015	\$ 475.982.761,50	
2	22/01/2016	\$ 138.828.305,44	
3	20/02/2016	\$ 138.828.305,44	
4	22/03/2016	\$ 138.828.305,44	
5	22/04/2016	\$ 138.828.305,44	
6	23/05/2016	\$ 138.828.305,44	
	23/06/2016	\$ 138.828.305,44	
	24/07/2016	\$ 138.828.305,44	
	24/08/2016	\$ 138.828.305,44	

VR TOTAL CONTRATO \$ 1.586.609.205,00

\$ 1.170.124.288,69

**VALOR PARCIAL**

**IVA**

**SEÑALIZACION PEATONAL**

AVISO DIRECCIONAL \$ 169.400.000,00 \$ 27.104.000,00  
 PANEL INTERPRET. ADOSADO \$ 13.068.000,00 \$ 2.090.880,00

**SEÑALIZACION ELEVADA**

BANDERA BIENV 7 MTS \$ 84.700.000,00 \$ 13.552.000,00  
 BANDERA TIPO INVIAS \$ 21.780.000,00 \$ 3.484.800,00  
 LAMA PARA BANDERA \$ 9.292.800,00 \$ 1.486.848,00  
 TABLERO PASAVIAS \$ 23.232.000,00 \$ 3.717.120,00  
 TABLERO BANDERA \$ 4.356.000,00 \$ 696.960,00  
 PASAVIAS 12 MTS \$ 18.150.000,00 \$ 2.904.000,00  
 PASAVIAS 24 MTS \$ 21.780.000,00 \$ 3.484.800,00

**SUMINISTRO**

TOTEM CON CIMENTACION MOD \$ 23.038.688,00 \$ 3.686.190,08  
 MONOLITO CIMENTACION MOD \$ 60.885.584,00 \$ 9.741.693,44  
 PANEL INTERPRET PIE \$ 12.127.248,00 \$ 1.940.359,68  
 PANEL INTERPRET MESA \$ 1.853.872,00 \$ 296.619,52  
 BANDERA 4 X 1,5 \$ 273.890.955,00 \$ 43.822.552,80  
 SEÑAL DIRECCIONAL 4 MODUL \$ 186.742.861,00 \$ 29.878.857,76  
 BANDERAS DOBLES 7 MTS \$ 12.684.764,00 \$ 2.029.562,24  
 BANDERAS DOBLES 4 MTS \$ 9.770.798,00 \$ 1.563.327,68

**VALOR PARCIAL**

**A.I.U.**

**INSTALACION SEÑALES**

TRANSP. INSTAL SEÑAL PEAT \$ 27.007.200,00 \$ 45.531.831,49  
 TRANSP. INSTAL SEÑAL VEHIC \$ 58.685.000,00 \$ 45.531.831,49

**VALOR PARCIAL**

**A.I.U.**

**INSTALACION SEÑALES**

TRANSPORTE MATERIALES \$ 45.000.000,00 \$ 45.531.831,49  
 LOCALIZACION REPLANTEO \$ 84.043.740,00 \$ 45.531.831,49  
 APIQUES HASTA 4 MTS \$ 374.343,00 \$ 45.531.831,49  
 AJUSTES \$ 73.792,00 \$ 45.531.831,49

1.313.418.216,00  
183.878.550  
13.134.182  
65.670.911  
10.507.346  
273.190.989


ACUMULADO	EJECUTADO		
	MES	SEMANAL	ACUMULADO
	\$ -		\$ -
\$ 475.982.761,50	\$ 475.982.761,50	\$ -	\$ 475.982.761,50
\$ 614.811.066,94	\$ -		\$ 475.982.761,50
\$ 753.639.372,38	\$ -		\$ 475.982.761,50
\$ 892.467.677,81	\$ -		\$ 475.982.761,50
\$ 1.031.295.983,25	\$ -		\$ 475.982.761,50
\$ 1.170.124.288,69	\$ 358.674.952,30	\$ -	\$ 834.657.713,80
\$ 1.308.952.594,13	\$ -	\$ -	\$ 834.657.713,80
\$ 1.447.780.899,56	\$ -	\$ -	\$ 834.657.713,80
\$ 1.586.609.205,00	\$ -	\$ -	

TOTAL		DISEÑO, FABRICACION, TRANSPORTE E INSTALACION	
\$ 196.504.000,00	12%		3,10%
\$ 15.158.880,00	1%		0,24%
\$ 98.252.000,00	6%		1,55%
\$ 25.264.800,00	2%		0,40%
\$ 10.779.648,00	1%		0,17%
\$ 26.949.120,00	2%		0,42%
\$ 5.052.960,00	0,32%		0,08%
\$ 21.054.000,00	1%		0,33%
\$ 25.264.800,00	2%		0,40%
\$ 26.724.878,08	2%		0,42%
\$ 70.627.277,44	4%		1,11%
\$ 14.067.607,68	1%		0,22%
\$ 2.150.491,52	0,14%		0,03%
\$ 317.713.507,80	20%		5,01%
\$ 216.621.718,76	14%		3,41%
\$ 14.714.326,24	1%		0,23%
\$ 11.334.125,68	1%		0,18%
\$ 72.539.031,49	5%		2,29%
\$ 104.216.831,49	7%		3,28%
\$ 90.531.831,49	6%		
\$ 129.575.571,49	8%		
\$ 45.906.174,49	3%		
\$ 45.605.623,49	3%		
\$ 1.586.609.205			






512392789 153717837 358674952

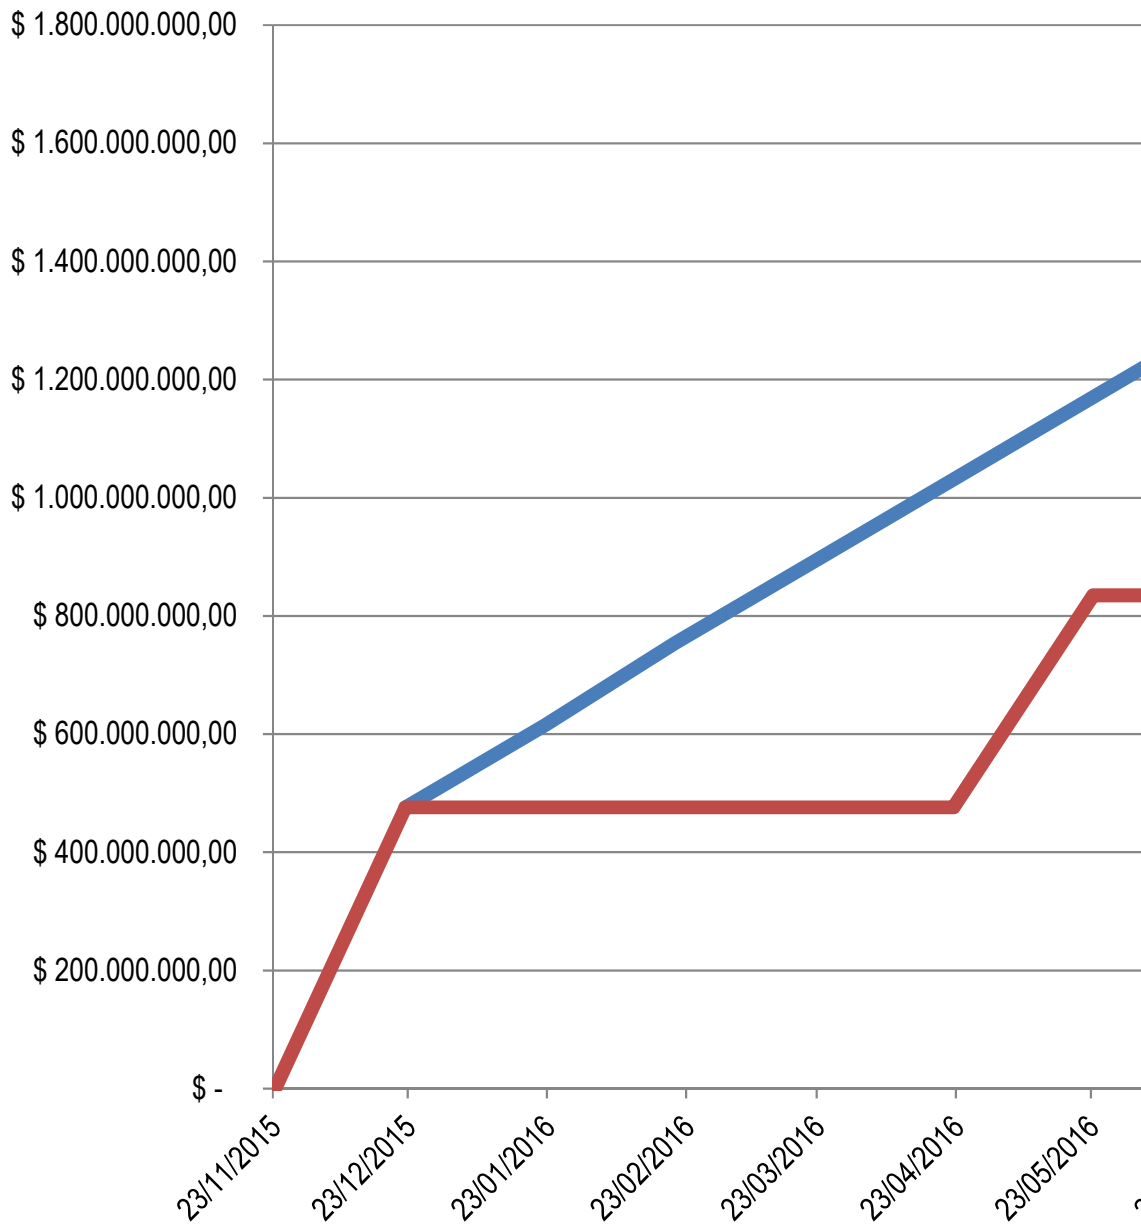



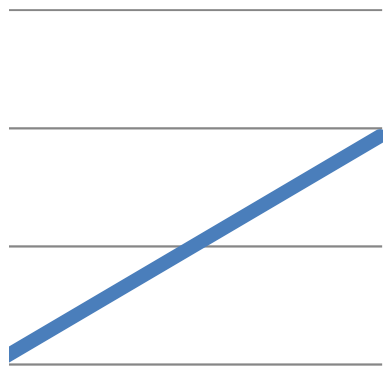

Programado  
Ejecutado

23/06/2016  
23/07/2016  
23/08/2016
